C.S. € 50.000.000,00 i.v. Reg.Impr.Rn, C.F. e P.I. 00126480409 R.E.A.72510 RN M/RN 005359




Necessary Activities for the machine installation ref. AA2/003277 REM-PILOT

Dear Sir(s),

This is the list of the necessary activities to carry out for the properly functioning of the machine. Pls, by fax +39(0)541700285 or by email edavoli@scmgroup.com send back this form with stamp and signature as your agreement of what Morbidelli-REM needs before the arrival of the technician. Pls, be informed that Morbidelli-REM will charge any delay due to the no-respect of the followings points:

✓ Machine body and its mechanics parts box put in a free area prepared for the installation that grants the <u>positioning according to the following layout</u>:

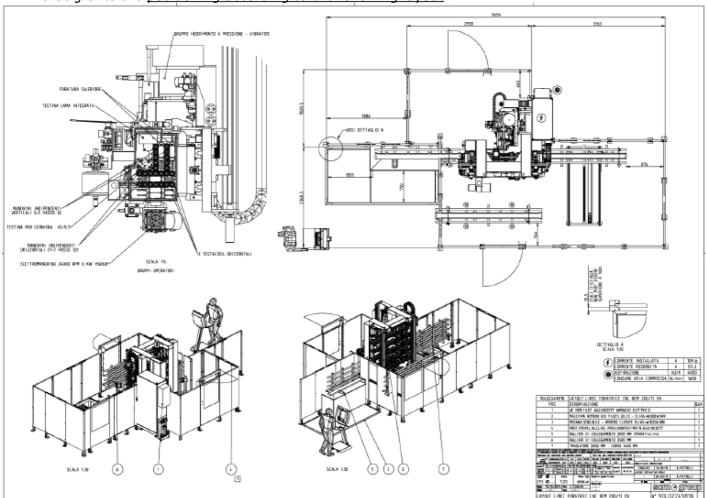

- ✓ Availability of a forklift (and its driver) + steel chains to hang up and move the machine
- ✓ <u>Electrical Connections</u> must be ready accordingly to the details in the layout **IN(A) 63,57**
- ✓ <u>Dust Extraction Connections</u> must be ready accordingly to the details in the layout
- ✓ Pneumatic Connections must be ready accordingly to the details in the layout
- → air must be without its condenses and other particles in suspension
- ✓ Availability of different typologies of <u>materials and tools for tests</u>
- ✓ Availability of at least one customer's operator always present with the Morbidelli-REM engineer

THE CUSTOMER CONFIRMS THAT WHAT ABOVE REQUIRED IS CARRIED OUT FOR THE INSTALLATION BEFORE THE ARRIVAL OF OUR TECHNICIAN

DATF /	/	STAMP AND SIGNATURE:	
